

# Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

|               |                                                     |
|---------------|-----------------------------------------------------|
| Date          | 03 October 2026                                     |
| Team ID       | 6aba11b55015c35b98631d18                            |
| Project Name  | Standard Laptop Procurement Automation (ServiceNow) |
| Maximum Marks | 5 Marks                                             |

## Product Backlog, Sprint Schedule, and Estimation (4 Marks)

| Sprint   | Functional Requirement (Epic) | User Story Number | User Story / Task                                                                                               | Story Points | Priority | Team Members |
|----------|-------------------------------|-------------------|-----------------------------------------------------------------------------------------------------------------|--------------|----------|--------------|
| Sprint-1 | Service Catalog               | USN-1             | As an admin, I can create the Standard Laptop catalog item with required variables                              | 5            | High     |              |
| Sprint-1 | Service Catalog               | USN-2             | As a user, I can submit a Standard Laptop request from the Service Portal so a Requested Item (RITM) is created | 3            | High     |              |
| Sprint-1 | Approvals                     | USN-3             | As a manager, I receive the request for approval when a RITM is created                                         | 5            | High     |              |
| Sprint-1 | Approvals                     | USN-4             | As an approver, I can approve or reject the laptop request                                                      | 3            | High     |              |
| Sprint-1 | Approvals                     | USN-5             | As a requester, I am notified of the approval outcome                                                           | 4            | Medium   |              |
| Sprint-2 | Flow Designer                 | USN-6             | As an admin, I can create a flow triggered on the Requested Item                                                | 5            | High     |              |
| Sprint-2 | Flow Designer                 | USN-7             | As the system, I check that approval state is "Approved" before proceeding                                      | 3            | High     |              |
| Sprint-2 | Flow Designer                 | USN-8             | As the system, I auto-create a Catalog Task when the request is approved                                        | 5            | High     |              |
| Sprint-2 | Flow Designer                 | USN-9             | As the system, I assign the Catalog Task to the Hardware group                                                  | 5            | High     |              |
| Sprint-2 | Flow Designer                 | USN-10            | As a hardware member, I see request details (requester, item, RITM) in the task description                     | 2            | Medium   |              |
| Sprint-3 | Task Fulfillment              | USN-11            | As a hardware member, I can see the assigned task in my group queue                                             | 3            | High     |              |
| Sprint-3 | Task Fulfillment              | USN-12            | As a hardware member, I can configure the laptop and update work notes                                          | 5            | High     |              |
| Sprint-3 | Task Fulfillment              | USN-13            | As a hardware member, I can close the task and the RITM updates accordingly                                     | 5            | High     |              |
| Sprint-3 | Notifications                 | USN-14            | As the Hardware group, I am notified when a new task is created                                                 | 3            | Medium   |              |
| Sprint-3 | Approvals                     | USN-15            | As a requester, if my request is rejected, no task is created and the RITM is closed                            | 4            | Medium   |              |
| Sprint-4 | Testing                       | USN-16            | As a tester, I can run end-to-end tests (request, approval, task, closure)                                      | 5            | High     |              |
| Sprint-4 | Testing                       | USN-17            | As a developer, I can verify flow execution logs and fix errors                                                 | 5            | Medium   |              |
| Sprint-4 | Deployment                    | USN-18            | As an admin, I can move the update set to the target instance                                                   | 5            | High     |              |
| Sprint-4 | Documentation                 | USN-19            | As a stakeholder, I get documentation and a demo of the solution                                                | 5            | Low      |              |

Project Tracker, Velocity & Burndown Chart (4 Marks)

| Sprint   | Total Story Points | Duration | Sprint Start Date | Sprint End Date (Planned) | Story Points Completed (as on Planned End Date) | Sprint Release Date (Actual) |
|----------|--------------------|----------|-------------------|---------------------------|-------------------------------------------------|------------------------------|
| Sprint-1 | 20                 | 6 Days   | 05 Oct 2026       | 10 Oct 2026               | 20                                              | 10 Oct 2026                  |
| Sprint-2 | 20                 | 6 Days   | 12 Oct 2026       | 17 Oct 2026               |                                                 |                              |
| Sprint-3 | 20                 | 6 Days   | 19 Oct 2026       | 24 Oct 2026               |                                                 |                              |
| Sprint-4 | 20                 | 6 Days   | 26 Oct 2026       | 31 Oct 2026               |                                                 |                              |


Velocity

Sprint duration = 6 days, team velocity = 20 story points per sprint.

Average Velocity (AV) = velocity / sprint duration = 20 / 6 = 3.33 story points per day

Burndown Chart

Total work = 80 story points over 24 days (4 sprints x 6 days). Ideal burndown below; actual line to be updated at each sprint end.

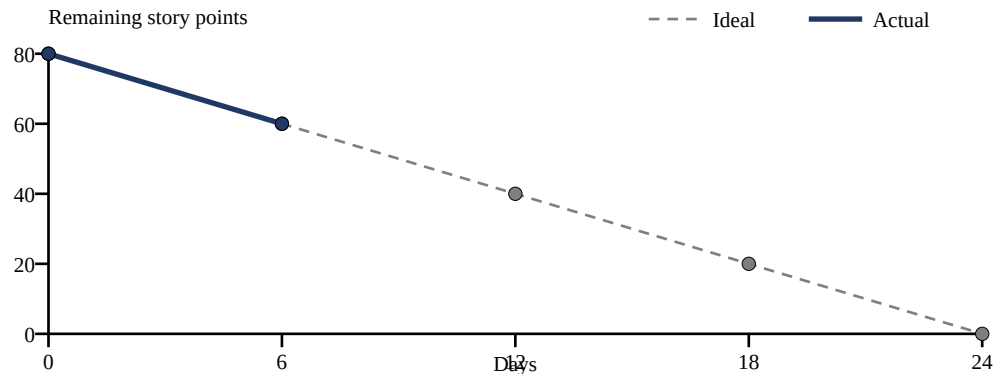

| Sprint end | Day | Ideal remaining | Actual remaining |
|------------|-----|-----------------|------------------|
| Start      | 0   | 80              | 80               |
| Sprint-1   | 6   | 60              | 60               |
| Sprint-2   | 12  | 40              |                  |
| Sprint-3   | 18  | 20              |                  |
| Sprint-4   | 24  | 0               |                  |
